


Solomon Islands Urban Water Supply and Sanitation Sector Project

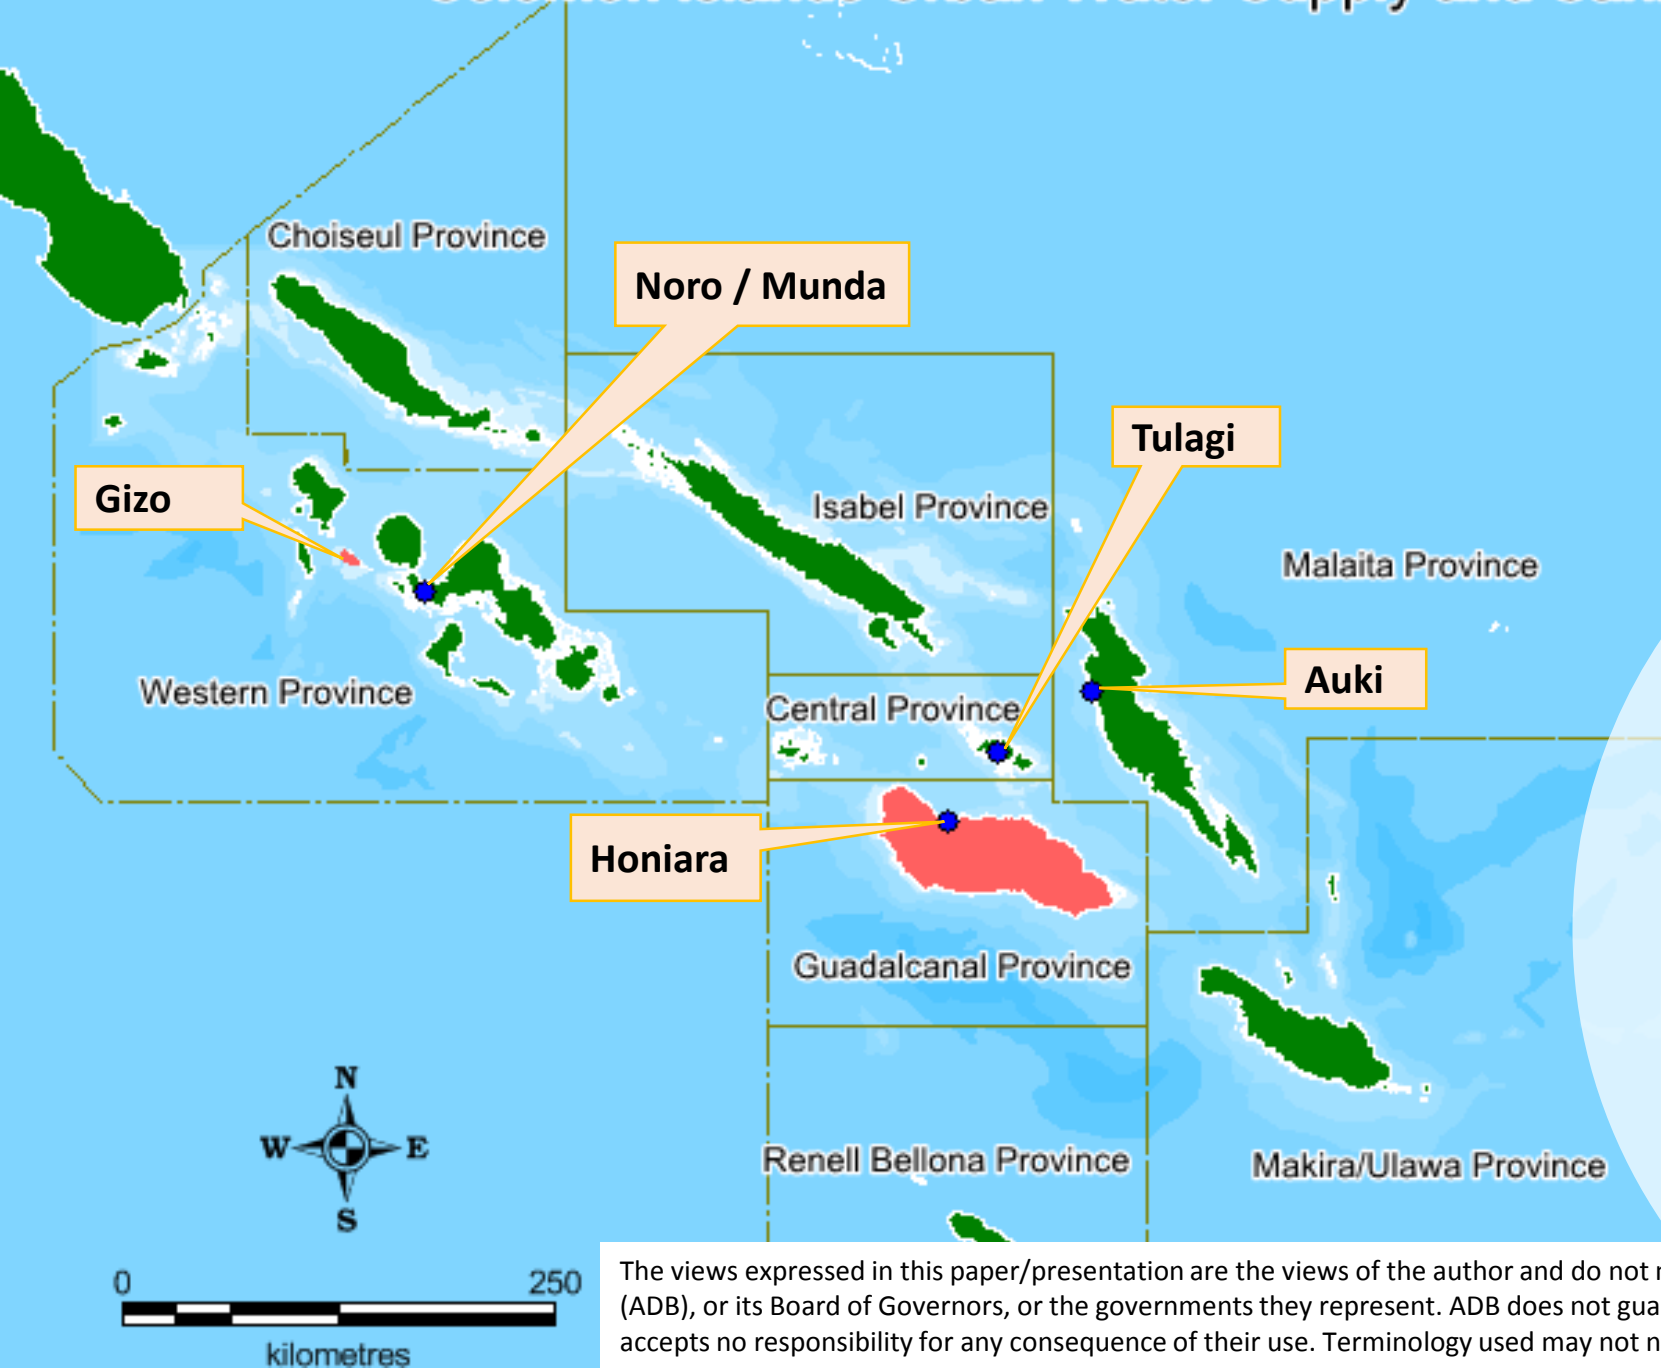

Project Readiness Financing:

A Case study

The views expressed in this paper/presentation are the views of the author and do not necessarily reflect the views or policies of the Asian Development Bank (ADB), or its Board of Governors, or the governments they represent. ADB does not guarantee the accuracy of the data included in this paper/presentation and accepts no responsibility for any consequence of their use. Terminology used may not necessarily be consistent with ADB official terms.



Project Background

UWSSSP will deliver improved water supply and sanitation services to urban centers in Solomon Islands.

- Project concept approved - Oct 2017
- Project preparation consultants fielded - Feb 2018
- Preparation completed – Mar 2019
- Board Approval – Sep 2019
- Project financing - \$92M (including counterpart of \$19M)
- Financing partners – ADB, EU, WB
(GCF and GEF applications being prepared – additional finance)
- Project duration – 8 years.
- Geographical coverage – 6 urban centers.



Project Readiness Financing - Basic Data

- PDA grant stand-alone request - Feb 2018
- PDA retired 30 Jun 2018 and replaced with PRF Oct 2018.
- UWSSSP PRF interdep review - Sep 18
- PRF grant negs - Nov 18
- PRF grant (\$3M) approval - Dec 2018.
- PRF effectiveness – Feb 2019.
- PRF completion date – 21 Dec 2020



Project Readiness Financing - Outputs

Output 1: Core subprojects and selected candidate subprojects are successfully procured

- surveys
- detailed engineering design
- Preparation of bidding documents
- Procurement support

Delivered by consulting firm.



Project Readiness Financing - Outputs

Output 2: The capacity of Solomon Water to manage and deliver the project is strengthened

- international project manager
- international water utility network specialist
- international contracts manager
- national resettlement specialist
- community liaison and communications specialist.

Individual consultants to strengthen PMU and to assist preparation of safeguard plans and community engagement.



Project Readiness Financing - Progress

Output 1:

- PRF consultants recruited under advance action and fielded in Feb 2019
- scope expanded to include feasibility studies for UWSSSP candidate subprojects
- solid overall progress
- bidding documents for most packages completed in Oct 19.



Project Readiness Financing - Progress

Output 2:

- Recruitment of individual consultants delayed



Project Readiness Financing - Issues

- processing delayed due to hiatus between retirement of PDA and approval of PRF instruments.
- new guidelines and procedures (e.g. templates) were untested – changes to templates during preparation of PRF Paper and PAM.
- “learning by doing”.
- PRF grant could have been larger given changes to scope of Output 1.
- PRF duration may be too short.
- exclusion of downstream project implementation assistance services could be problematic.
- PMDCs unwilling to borrow for PRF.

A photograph of a body of water, likely a lake or sea, with a ship visible on the horizon under a clear blue sky. The water is calm, and the ship is a small, dark silhouette against the horizon line.

Project Readiness Financing - Benefits

- improved project readiness and faster project implementation.
- improved ownership and buy-in prior to project approval (beneficiaries money).
- reduced reliance on TA funds for project preparation

Overall, PARD PRF experience good. 2 urban PRF grants in PARD's 2019 pipeline.
