The views expressed in this presentation are the views of the author/s and do not necessarily reflect the views or policies of the Asian Development Bank, or its Board of Governors, or the governments they represent. ADB does not guarantee the accuracy of the data included in this presentation and accepts no responsibility for any consequence of their use. The countries listed in this presentation do not imply any view on ADB's part as to sovereignty or independent status or necessarily conform to ADB's terminology.

# Access to ADB Business Opportunities –Identifying Packages for Goods, Works and Consultancy Services

## ADB Business Opportunities Seminar 28 April 2025

### Mohammed Zulyaminayn

Principal Procurement Officer ADB Bangladesh Resident Mission **Md. Rasel Parvez** 

Procurement Officer ADB Bangladesh Resident Mission

# **Why pursue ADB-Financed Contracts?**





Gateway to new opportunities in fast growing emerging economies across multiple sectors



Availability of funds are assured



Internationally accepted procurement procedures: transparent & fair for all




Risks related to integrity of procurement processes mitigated through ADB oversight


28 April 2025


# How to Identify Opportunities for Goods/Works and Consulting Services


Future opportunities – in Future, e.g. Q4/2025 or Q1-Q4/2026

### Immediate opportunities – Now or Soon, e.g. Q2/2025, Q3/2025

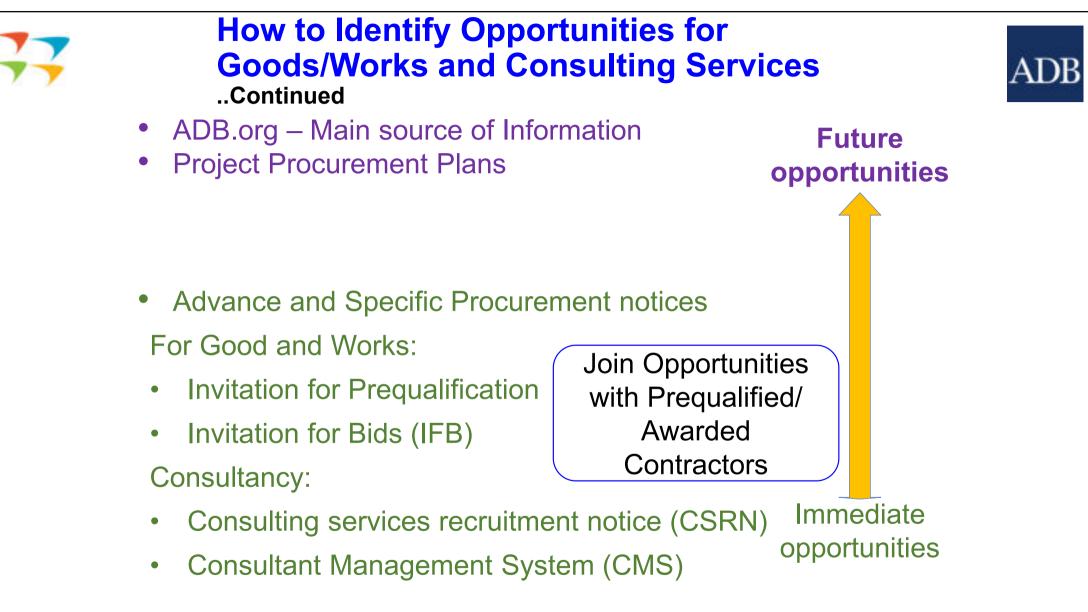

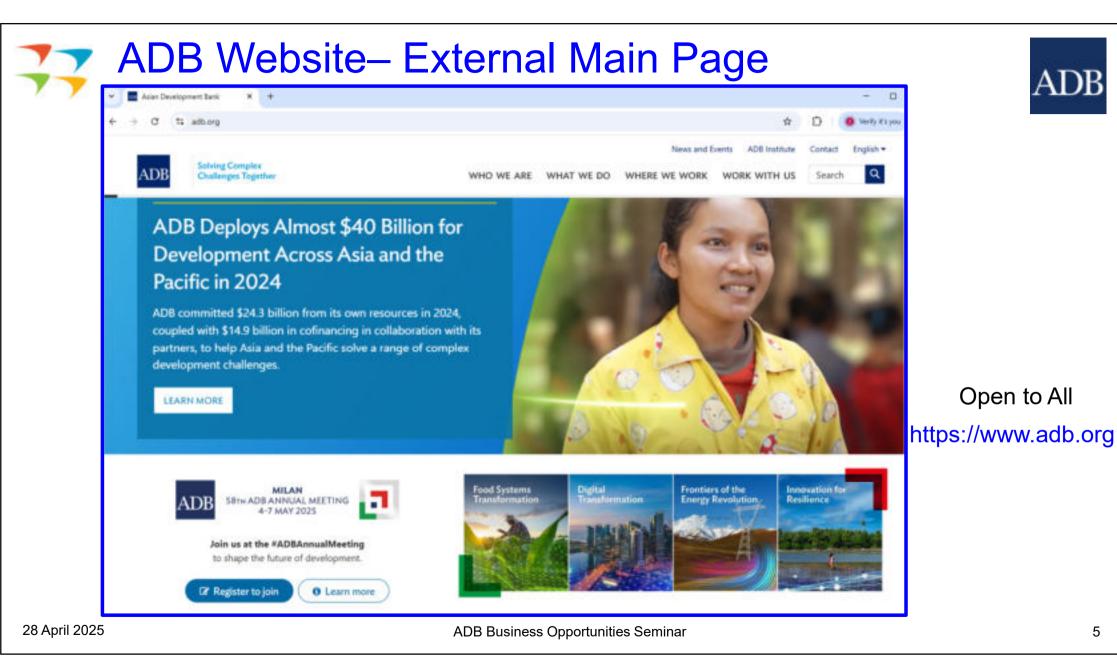



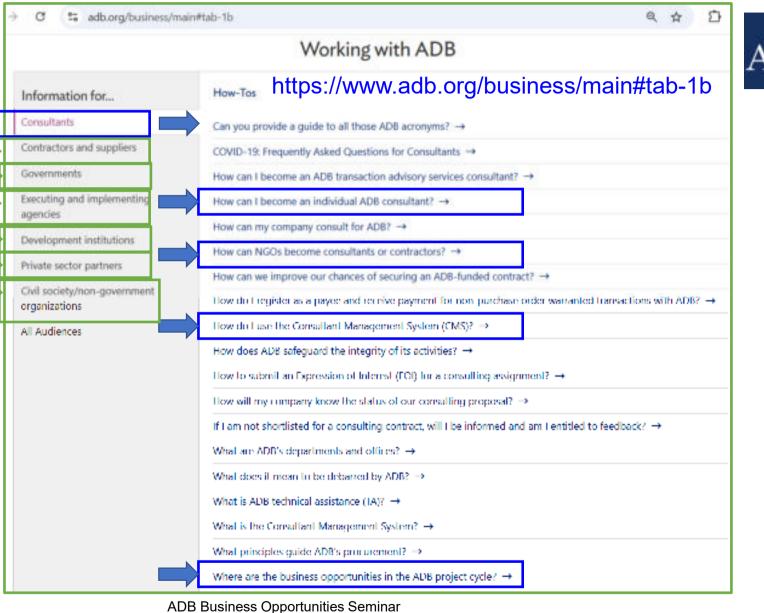

28 April 2025

77

Working with ADB– Contractors and suppliers (Open to All)

• Work with Us > Working with ADB	https://www.adb.org/business/main#tab-1b Working with ADB
aformation for onsultants ontractors and suppliers overnments ecuting and implementing pencies evelopment institutions ivale socior partners vil society/non-government ganizations Audiences	How-Tos Can you provide a guide to all those ADB acronyms? → How can I become an ADB supplier? (corporate procurement) → How can NGOs become consultants or contractors? → How can NGOs become consultants or contractors? → How do I register as a payee and receive payment for non-purchase order warranted transactions with ADB? → How do I register as a payee and receive payment for non-purchase order warranted transactions with ADB? → How dos ADB safeguard the integrity of its activities? → What are ADB's departments and offices? → What are the eligibility requirements for subcontractors working for contractors on ADB-financed projects? → What are the eligibility requirements for bidding for contracts under ADB-financed projects? → What does it mean to be debarred by ADB financed projects? → What does it mean to be debarred by ADB financed projects? → What is ADB technical assistance (IA)? → What is ADB technical assistance (IA)? → When and how are bidders informed about the awarding of the contract? → Where are the business opportunities in the ADB project cycle? → Where can I find ADD's standard bidding documents? →

28 April 2025

7



Results of ADB-Supported Operations

Results achieved are aggregate amounts of outputs and outcomes from operations reported in project completion reports and extended annual review reports circulated for the year.

Bangladesh Facts ADB's Work in Bangladesh

ADB has been a major source of external assistance to Bangladesh, providing an average of \$2 billion per year since 2016. ADB assistance is aligned with Bangladesh's Eighth Five-Year Plan. 2021–2025, and Perspective Plan. 2021–2041.

To date, ADB has committed 726 public sector loans, grants, and technical assistance totaling \$31.8 billion to Bangladesh. ADB's current sovereign portfolio in Bangladesh includes 75 loans and 4 grants worth \$13 billion.

More on ADB's work in Bangladesh
 Country Partnership Strategies

🗧 Download Country Brief

28 April 2025

# ADB Bangladesh–Active & Proposed Projects




9

https://www.adb.org/where-we-work/bangladesh

rojects ADB-Administered Funds Supporting Bangladesh			
Featured	Approved/Active	Proposed	
	55112-001   17 MAR 2025 Mainstreaming Green, Resilient, and Inclusive Approaches for Cities in Asia and the Pacific	49258-003 Dhaka Mass Rapid Transit Development Investment Project (Line 5, Southern Route)	
AND AND A TANK ON A DAY OF A DAY OF A DAY	58071-001   06 MAR 2025 Strengthening Regulatory Ecosystem and Manufacturing for Vaccines, Therapeutics, and	36200-024 Second Small and Medium-Sized Enterprises Development Project (Phase 2)	
THE NT H	Diagnostics in Asia and the Pacific (REVITALIZE) 58250-001   20 DEC 2024 Scaling Up Financing and Technology Innovations to Promote Solar Energy in South Asia	57182-001 NextGen Secondary Education Program	
1 The Date of the State of the		53303-002 2024 International Comparison Program for As	
and the second sec	58064-001   18 DBC 2024	and the Pacific	
Land Leasing: A Versatile Instrument to Minimize and Mitigate Involuntary Resettlement Impacts - Experience	Transport Interventions to Boost Trade and Tackle Climate Change in the South Asia Subregional Economic Cooperation Region	58076-001 Scaling Up Clean Air Actions for Better Health a Resilience	
in India and Bangladesh	58375-001   15 DEC 2024		
Land leasing is a versatile, voluntary instrument that helps avoid, minimize, and mitigate involuntary resettlement impacts in development interventions.	Enabling Participation in International Carbon Markets		


## **ADB Bangladesh–Knowing Project Stories** https://www.adb.org/countries/bangladesh/projects-results Bangladesh: Projects and Results PROJECT RESULT / CASE STUDY \ 07 JUN 2024 Land Leasing: A Versatile Instrument to Minimize and Mitigate Involuntary Resettlement Impacts - Experience in India and Bangladesh PROJECT RESULT / CASE STUDY J 24 MAR 2023 In Bangladesh, ADB Helped Build A Safer and Healthier Workplace for Women Garment Workers PROJECT RESULT / CASE STUDY | 01 APR 2022 Securing a Sustainable Water Resource for Dhaka PROJECT RESULT / CASE STUDY | 22 DEC 2021 ADB Helps Bangladesh on Road to Recovery from COVID-19 PROJECT RESULT / CASE STUDY I 10 FEB 2020 Emergency Assistance in Bangladesh PROJECT RESULT / CASE STUDY ) DE NOV 2018 Bangladesh: Throwing a Lifeline to Small Businesses



28 April 2025

ADB Business Opportunities Seminar

10

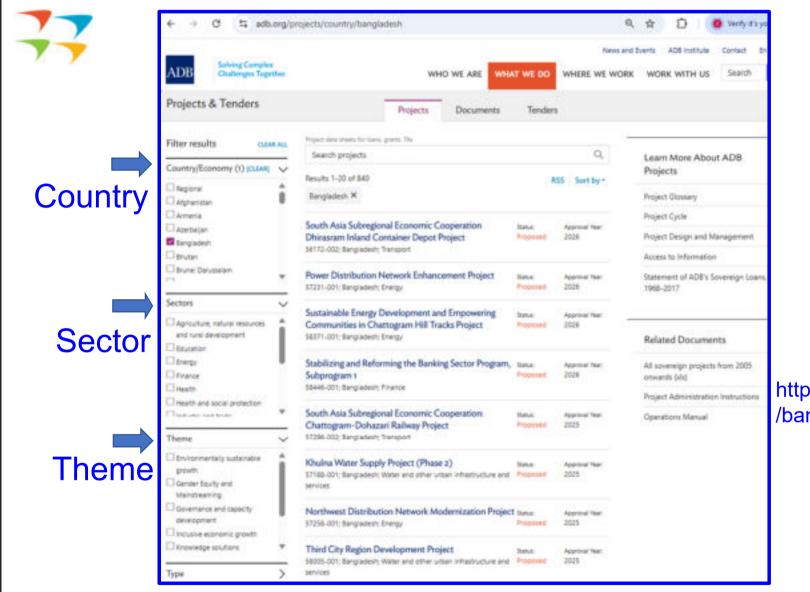




## Search ADB Website– Bangladesh Projects

https://www.adb.org/projects/country /bangladesh

28 April 2025

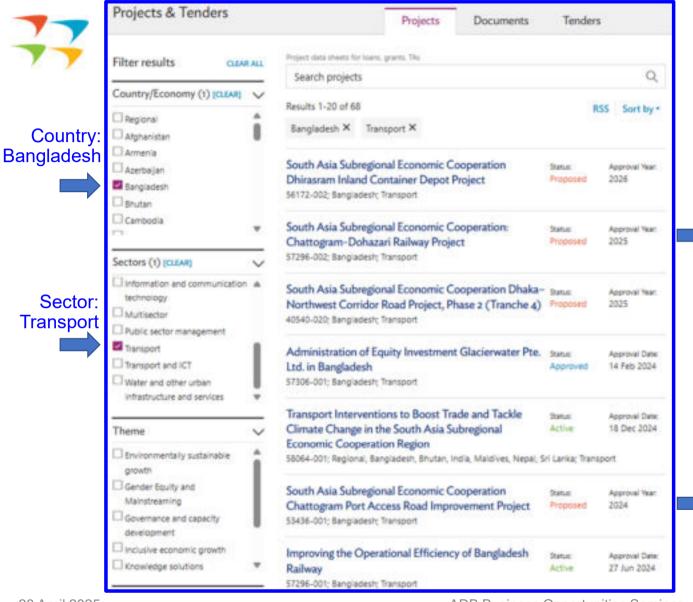

South Asia Subregional Economic Cooperation: Chattogram-Dohazari Railway Project 57296-002: Bangladesh: Transport: Proposed 2025

https://www.adb.org/projects/country /bangladesh/sector/transport-1064


South Asia Subregional Economic Cooperation Chattogram Port Access Road Improvement Project 53436-001: Bangladesh: Transport: Proposed 2024 ?

28 April 2025

ADB Business Opportunities Seminar

ADB



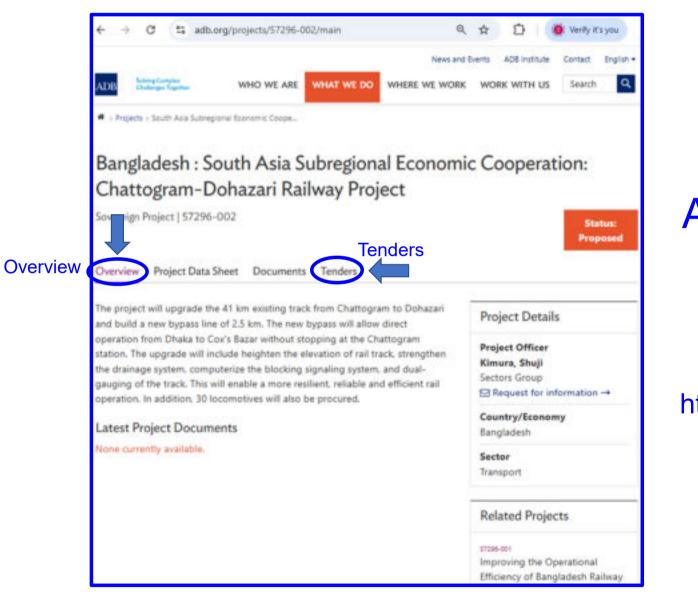

https://www.adb.org/ projects/57296-002/main

28 April 2025

ADB Business Opportunities Seminar

13

https://www.adb.org/ projects/57296-002/main

Bangladesh : South Asia Subregional Economic Cooperation: Chattogram-Dohazari Railway Project


Sovereign P	roject   57296-002		Status: Proposed
Overview	Project Data Sheet	Tenders	

#### Tenders

Tender Title	Туре	Status	Posting Date	Deadline	_
Consultancy Services for Construction Supervision	Firm - Consulting	Active	05 Mar 2025	02 May 2025	Tend
57296-002 BAN: South Asia Subregional Economic Cooperation []	Advance	Proposed	30 Oct 2024		
Chattogram-Dohazari Railway Project	Notice				





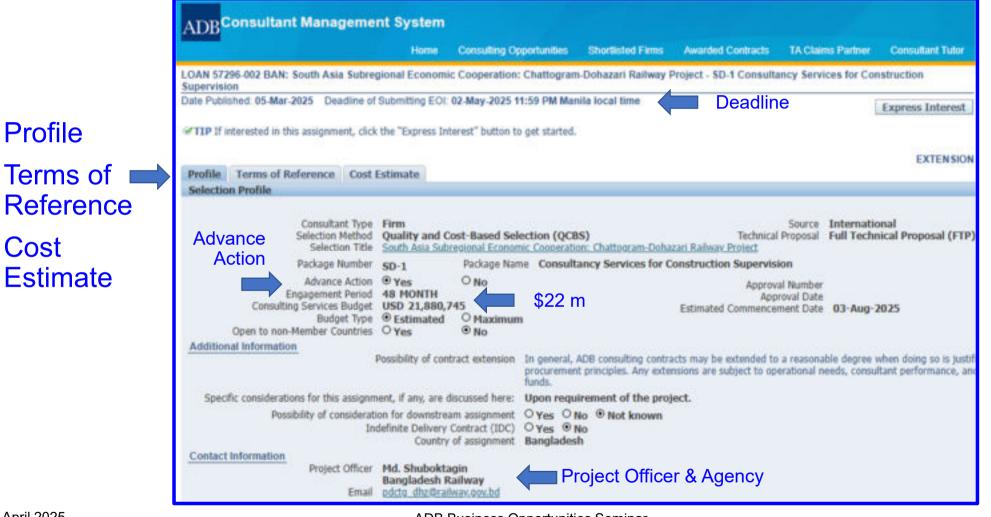


28 April 2025

https://www.adb.org/ projects/57296-002/main

Bangladesh : South Asia Subregional Economic Cooperation: Chattogram-Dohazari Railway Project

Sovereign Project | 57296-002 Status: Proposed **Tenders Project Data Sheet** Overview Documents Tende Tenders **Tender Title Posting Date** Type Deadline Status **Consultancy Services for Construction Supervision** 02 May Active 05 Mar 2025 Firm -Consulting 2025 Proposed 30 Oct 2024 57296-002 BAN: South Asia Subregional Economic Cooperation D Advance Chattogram-Dohazari Railway Project Notice **Advance Action** 28 April 2025 ADB Business Opportunities Seminar



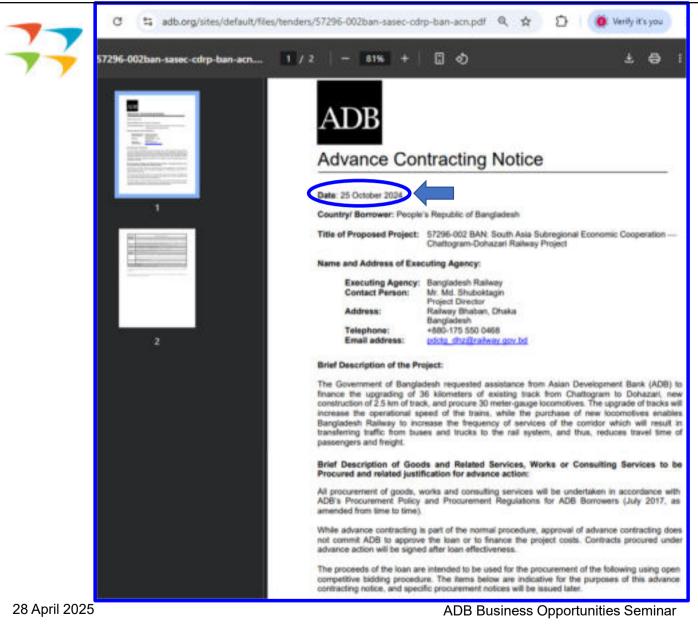


South Asia Subregional Economic Cooperation: Chattogram-Dohazari **Railway Project** 57296-002: Bangladesh: **Transport: Proposed 2025** 

https://www.adb.org/sites/d efault/files/tenders/57296-002ban-sasec-cdrp-banacn.pdf

Package Number	General Description
Goods	
GD-1	Procurement of 30 meter-gauge diesel electric complete locomotives including drawing, spare parts, tools and plants, catalogue, capital and maintenance spares overseas training, service engineers, study tour, etc.
GD-2	Supply and commissioning of broad-gauge ballast tamping machine
GD-3	Procurement of two (2) motor trolley
GD-4	Procurement of permanent way tools and equipment, and supply and commissioning of Ultrasonic Rail Flaw Detection System
GD-5	Procurement of one (1) gang car
Works	
WD-1	All civil works for conversion of meter gauge track to dual gauge track from Chattogram to Gumdandi and construction of dual gauge line from Pahartali to Jhautala (31.41 km, main & loop line) including signaling and telecommunication with other allied works
WD-2	All civil works for conversion of meter gauge track to dual gauge track from Gumdandi to Dohazari with other allied works (31.47 km, main & loop line)
Consulting	g services
SD-1	Construction supervision consultant
t is expected onwards. nterested bi	t that bidding for the various contracts under the project will commence from Q4 20 dders from ADB member countries who wish to obtain additional information m
contact the a	bovementioned officer.
	ADB Business Opportunities Seminar

ADB

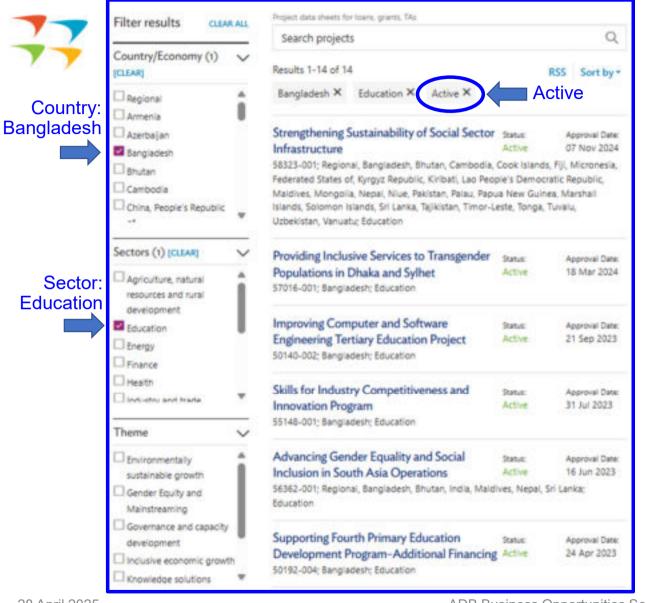



Improving Computer and Software Engineering Tertiary Education Project 50140-002: Bangladesh Status: Active

https://www.adb.org/projects/country /bangladesh

https://www.adb.org/projects/country /bangladesh/sector/education-1058/status/active-1367

28 April 2025

ADE Overview	Overview Project Data Sheet Documents Stories Tenders	Ne DO WHERE WE W Tenders WW.adb.org/p computer science ree selected	work work with us rojects/50140-00 Project Details	ontact English • Search Q 02/main
	entrepreneurial spirit. The project will provide cutting-edge education up support facilities, quality curriculum design, and academic staffing international standards and industry requirements. It will introduce a scheme to promote industry-relevant and interdisciplinary research a	n, research and start- aligned with competitive grant nd development	Project Officer Hayashi, Ryotaro Sectors Department 3 Request for information	
	(R&D) initiatives. The grant scheme will help the universities and indu new digital technology solutions for economic and social issues.	stry partners develop	Country/Economy Bangladesh	Procurement
	Latest Project Documents		Sector	Plan
	Title	Date	Education	& Tenders
	Improving Computer and Software Engineering Tertiary Education Project: Updated Project Administration Manual	Mar 2025	Related Projects	
Latest Procurement Plan	Improving Computer and Software Engineering Tertiary Education Project: Procurement Plan	Jan 2025	seras-cor Innovations in Tertiary Edu	
Signed Agreement	Loan Agreement (Ordinary Operations [Concessional]) for Loan 4348-BAN: Improving Computer and Software Engineering Tertiary Education Project	Nov 2023	Competitiveness in Inform Technology Project	nauon
28 April 2025	ADB Business Op	portunities Seminar		20

ADB Website-Ban		ADB
Improving Computer and Software Engineering Tertiary Education Project: Procurement Plan Procurement Plans   January 2025 SHARE THIS PAGE		of project: Goods, Works & proved & updated regularly I Cost, Tentative Advertisement
Download (7mm \$127 KB) Download (Open to All)		REMENT PLAN Basic Data
Procurement plans describe and update the procurement of major goods, works and conservices either ongoing or expected to take place related to a project or program.	Project Name: Improving Computer and Software E	
	Project Number: 50140-002	Approval Number: 4348
This document dated 28 January 2025 is provided for the ADB project 50140-002 in	Country: Bangladesh	Executing Agency: Ministry of Education
Bangladesh. Project Number 50140-002 Countries Bangladesh includes Packages Subjects	\$114 m Project Financing Amount: US\$ 114,000,000 ADB Financing: US\$ 100,000,000 Cofinancing (ADB Administered): Non-ADB Financing: US\$ 14,000,000	Implementing Agency: Bangladesh University of Engineering and Technology, Jashore University of Science and Technology, University Grants Commission of Bangladesh, University of Dhaka Project Closing Date: 31 December 2028 Latest Procurement Plan
Education	Date of First Procurement Plan: 21 September	Date of this Procurement Plan: 28 January 2025,
	2023 Procurement Plan Duration 18 months	Related to COVID-19 response efforts: No
	Advance Contracting: Yes	Use of e-procurement (e-GP): Yes www.eprocure.gov.bd
28 April 2025	ADB Business Opportunities Seminar	21

## **Bangladesh Projects**-All **Procurement Plans**

https://www.adb.org/projects /documents/country/ban/doc type/Procurement%20Plans

Projects & Tender	s	Projects Documents Te	nders
Filter results curv	ALL	Procurement plans, reports, safeguards, etc.	0
Country/Economy (1)	~	Search projects Bangladesh Results 1-20 of 107 Procurement Plans	Q 5 Sort by *
Regional Armenia	î	Bangladesh X Procureme X	
🗆 Azerbaijan 🖾 Bangladesh 🗆 Bhutan		Chattogram Hill Tracts Inclusive and Resilient Urban Water Supply and Sanitation Project: Procurement Plan 51296-002; Bangladesh: Type: Procurement Plans	Document Date 15 Apr 2025
Cambodia	٣	Improving Computer and Software Engineering Tertiary Education Project: Procurement Plan 50140-002; Bangladesh; Type: Procurement Plans	Document Data 28 Jan 2025
Type (t) (CLEAR)	Y	Coastal Towns Climate Resilience Project: Procurement	Document Date:
Additional Financing (Cofinancing) Agreements	ô	Plan 55201-001; Bangladesh; Type: Procurement Plans	03 Jan 2025
Audit and Performance Evaluation Reports		Emergency Assistance Project: Procurement Plan 52174-001; Bangladesh; Type: Procurement Plans	Document Date 15 Sep 2024
Statements Cancellation Notices	Ŧ	Urban Primary Health Care Services Delivery Project: Procurement Plan 42177-013, 42177-024; Bangladesh; Type: Procurement Plans	Document Date: 09 Apr 2024
Language	V		
English .		COVID-19 Response Emergency Assistance Project: Procurement Plan 54173-001; Bangladesh; Type: Procurement Plans	Document Date: 09 Apr 2024
Year	>	services, and an entry the computation cars	
Apply		Vaccines, Therapeutics, and Diagnostics Manufacturing and Regulatory Strengthening Project: Procurement Plan 56289-001; Bangladesh; Type: Procurement Plans	Document Date 24 Jan 2024

**Improving Computer** and Software **Engineering Tertiary Education Project** (ICSETEP) 50140-002

Vaccines, Therapeutics, and **Diagnostics** Manufacturing and Regulatory Strengthening Project (VTDMRSP) 56289-001

28 April 2025

ADB Business Opportunities Seminar

22

	Project Procurement Plan: Template				
	PROCU	REMENT PLAN			
	B	asic Data			
Project	Project Name: Improving Computer and Software En	ngineering Tertiary Education Project			
	Project Number: 50140-002	Approval Number: 4348 Loan No.			
	Country: Bangladesh	Executing Agency: Ministry of Education			
	Project Financing Amount: US\$ 114,000,000 ADB Financing: US\$ 100,000,000	Implementing Agency: Bangladesh University of Engineering and Technology, Jashore University of Science and Technology, University Grants Commission of Bangladesh, University of Dhaka			
	Cofinancing (ADB Administered): Non-ADB Financing: US\$ 14,000,000	Project Closing Date: 31 December 2028			
Minimum			Last		
Time Span of Plan	Date of First Procurement Plan: 21 September 2023	Date of this Procurement Plan: 28 January 2025, Version 4	Update &		
	Procurement Plan Duration: 18 months	Related to COVID-19 response efforts: No	Version		
	Advance Contracting: Yes	Use of e-procurement (e-GP): Yes www.eprocure.gov.bd	NO.		
28 April 2025	ADB Business	Opportunities Seminar	23		

7	Project Procurement Pl Continued	an: Template
	Procurement of 0	Goods and Works
	Method	Comments
	Open Competitive Bidding (OCB) for Goods	Significant numbers of local suppliers particularly IT equipment supplier available in the country and the market is competitive. First one package per university and PMU and some selected high value contracts are subject to prior review. All other packages are subject to post-review sampling.
FQ for Goods	Request For Quotation for Goods	For readily available goods of small value and standard specifications. First one package per university and PMU are subject to prior review. All other packages are subject to post review sampling.
	Framework Agreements for Goods	For small items such as office supplies and consumables for PMU and PIUs (under government financing)
	Others for Goods	OCB w/ national advertisement for non-consulting services
CB (N)	Open Competitive Bidding (OCB) for Works	Adequate number of construction firms exist in the country with the required 'know-how' and expertise in construction of high-rise building and execution of large value contracts. The construction materials are also locally available and the market is competitive. OCB works packages are subject to prior review.
for Works	Request For Quotation for Works	For refurbishing, renovation of small value construction works. First one package per university and PMU are subject to prior review.
	Consulting	g Services
	Method	Comments
	Quality- and Cost-Based Selection for Consulting Firm	prior review Consulting
	Consultant's Qualification Selection for Consulting Firm	prior review Services
	Competitive for Individual Consultant	prior review OCI VICES

28 April 2025

-



# Project Procurement Plan: Template ..Continued



#### B. Lists of Active Procurement Packages (Contracts)

The following table lists goods, works, non-consulting and consulting services contracts for which the procurement activity is either ongoing or expected to commence within the procurement plan duration.

Goods and Works							
Package Number	General Description	Estimated Value (in US\$)	Procurement Method	Review	Bidding Procedure	Advertisement Date (quarter/year)	Comments
	•	•				•	
Consulting S	Consulting Services						
Package Number	General Description	Estimated Value (in US\$)	Selection Method	Review	Type of Proposal	Advertisement Date (quarter/year)	Comments

#### C. List of Indicative Packages (Contracts) Required Under the Project


The following table lists goods, works, non-consulting and consulting services contracts for which procurement activity is expected to commence beyond the procurement plan duration and over the life of the project (i.e., those expected beyond the current procurement plan duration).

Goods and Works							
Package Number	General Description	Estimated Value (in US\$)	Procurement Method	Review	Bidding Procedure	Comments	
Consulting Services							
Package Number	General Description	Estimated Value (in USS)	Selection Method	Review	Type of Proposal	Comments	

## **Bangladesh Projects**-**All Tenders**

https://www.adb.org/projects /tenders/country/bangladesh

Type

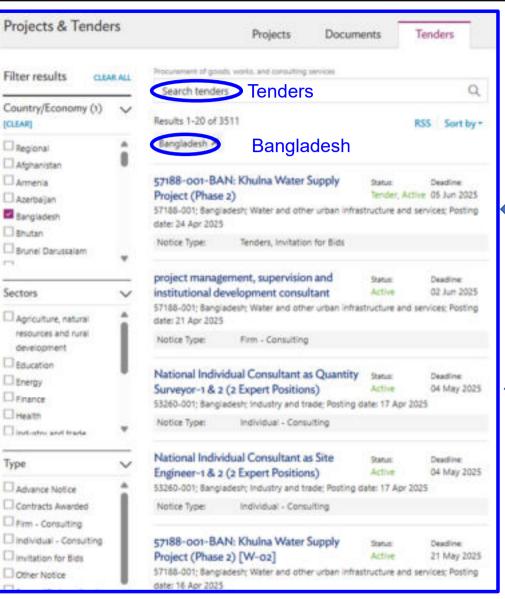

57188-001-BAN: Khulna Water **Supply Project** 

National Individual Consultant as Quantity Surveyor-1 & 2 (2 Expert Positions)

(Phase 2)

57188-001

 Advertisement in ADB.org depends on category & cost estimate

28 April 2025

# Large Project Procurement Plan: 2021 Example


Goods and W	/orks						
Package Number	General Description	Estimated Value (in US\$)	Procurement Method	Review	Bidding Procedure	Advertisement Date (quarter/year)	Comments
WP-06	Improvement of the Dhaka (Katchpur) - Sylhet National Highway (N2) into a 4-Lane Highway with Service Lane on Both Sides from Sherpur Bridge Toll Plaza to 7-Armed Police Battalion Headquarters, Lalabazar (Ch 186+700 to	283,592,227.97	OCB	Prior	152E	Q4 / 2021	Non-Consulting No Advertising: International No. Of Contracts: 3 Prequalification of Bidders: No Domestic Preference Applicable: No Advance Contracting:
		etitive Bio iew biddir		ment ar	nd Eva	luation	Yes Bidding Document: Large Works High Risk Contract:

- Prio **Reports**
- 1S2E = Single Stage, 2-Envelope (Technical and Price) Proposal)
- No. of Contracts = 3 (Three Lots under the package)

28 April 2025

• OC

### Large Project Procurement Plan: Sample from 2021 ..Continued

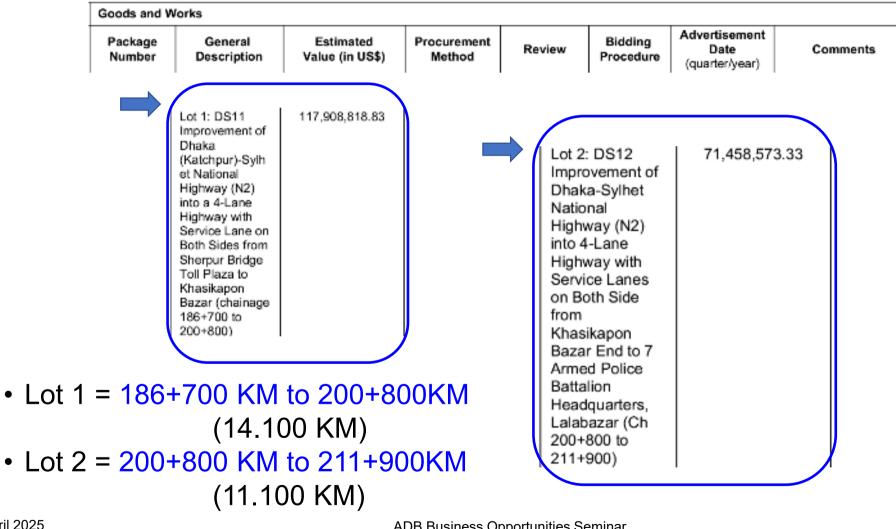

28 April 2025



### Large Project Procurement Plan: Sample from 2021 ..Continued


Goods and W	orks						
Package Number	General Description	Estimated Value (in US\$)	Procurement Method	Review	Bidding Procedure	Advertisement Date (quarter/year)	Comments
WP-05	Improvement of Dhaka (Katchpur)-Sylh et National Highway (N2) into a 4-Lane Highway with Service Lane on Both Sides from Square Textiles Land, Bahubal to Sadarghat Natun Bazar Jame Masjid to Sherpur Bridge Toll Plaza (chainage 151+000 to 186+700)	347,012,802.05	OCB	Prior	152E	Q4 / 2021	Non-Consulting Services: No Advertising: International No. Of Contracts: 2 Prequalification of Bidders: No Domestic Preference Applicable: No Advance Contracting: Yes Bidding Document: Large Works High Risk Contract:

- OCB = Open Competitive Bidding
- Prior = ADB will review bidding document and Evaluation Reports
- 1S2E = Single Stage, 2-Envelope (Technical and Price Proposal)
- No. of Contracts = 2 (Two Lots under the package)

28 April 2025

No

# Large Project Procurement Plan: Sample from 2021

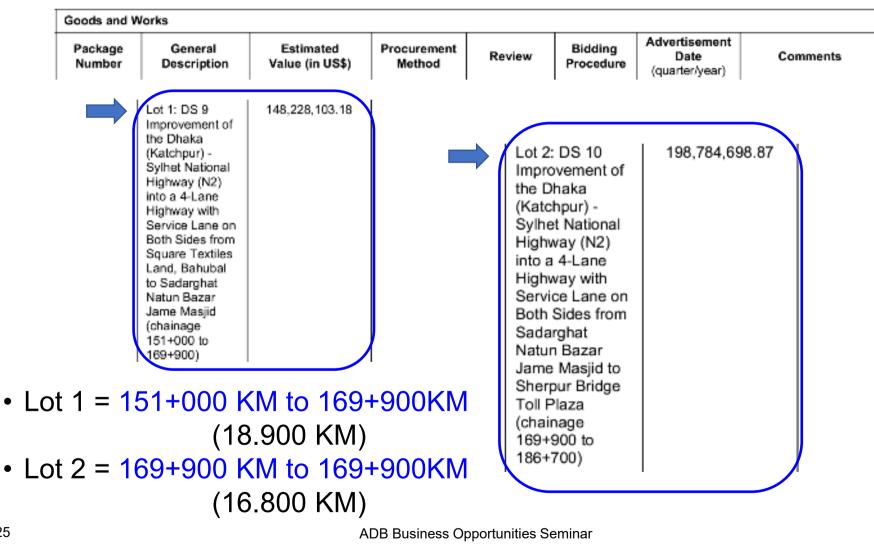

28 April 2025

ADB

30

## DB Active Tender Example–Bangladesh Water Supply



#### Invitation for Bids

	Date:	24 April 2025
Project 📥	Loan No. and Title:	57188-001-BAN: Khulna Water Supply Project (Phase 2)
	Contract No. and Title:	W-05: Construction of Clear Water Transmission Main including Mauri river and drain crossing including 2 years of operation and maintenance
Deadline 🗪	Deadline for Submission of Bids:	5 June 2025 at 15:00 hours (Bangladesh Standard Time)
Background	Bank (ADB) tow will be used for	epublic of Bangladesh has applied for financing from the Asian Development rard the cost of Khulna Water Supply Project (Phase 2). Part of this financing payments under the contract named above. Bidding is open to Bidders from countries of ADB.
Package Details	from eligible Bi Water Transmi	ater Supply and Sewerage Authority ("the Employer") invites sealed bids dders for the construction and completion of W-05: Construction of Clear ssion Main including Mauri river and drain crossing including 2 years of maintenance ("the Works").
	with ADB's Sin	tive bidding – International advertisement will be conducted in accordance gle-Stage: Two-Envelope bidding procedure and is open to all Bidders from s as described in the Bidding Document.
Key Qualifications 📥	<ol> <li>Only eligible Bi may participate</li> </ol>	dders with the following key qualifications defined in the Bidding Document in this bidding:
	(ii) Particip years i particip (iii) Demon million (iv) Comple	m average annual construction turnover <b>BDT 20 million</b> during the last five vation in at least one similar contact to the proposed works within the last <b>10</b> successfully or substantially completed where the value of the Bidder's ation exceeds <b>BDT 25 million</b> . strates total finance resources required equal to or above the <b>BDT 4.30</b> of or subject contact.
oril 2025	30001E	ADB Business Opportunities Seminar

57188-001 https://www.adb.org/sites/def ault/files/tenders/ban57188w-05-ifb.pdf

57188-001-BAN:


Khulna Water

**Supply Project** 

(Phase 2)

Internationally advertised OCB and >=\$1m posted in ADB.org

. .

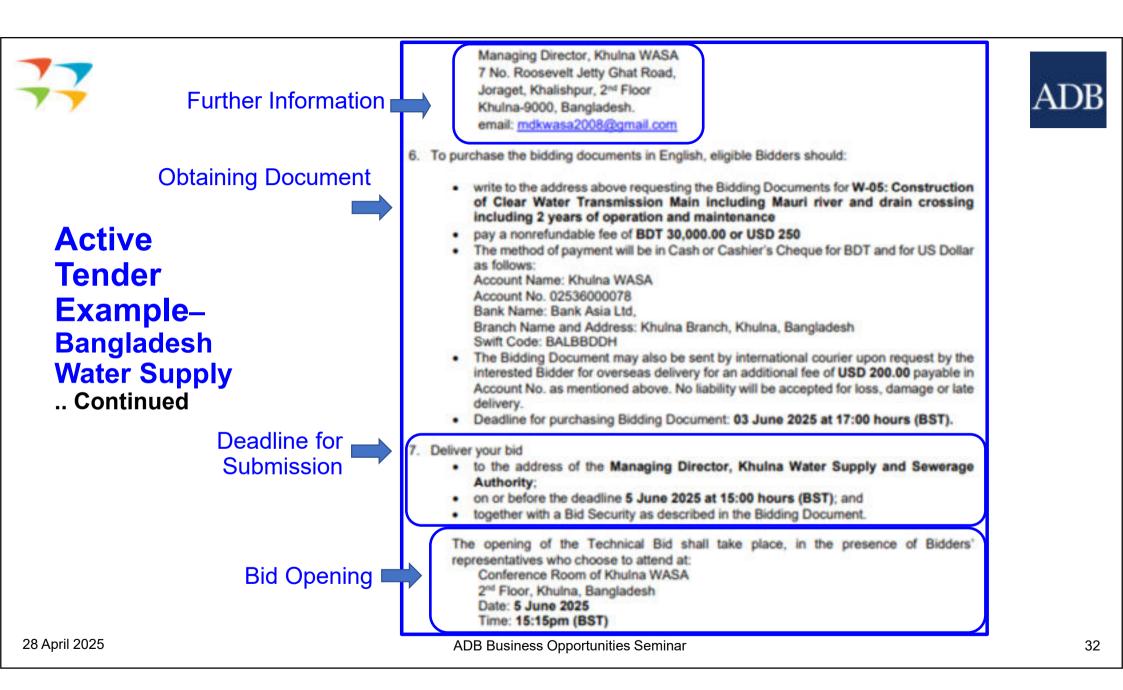

# 77

## ADB Sample High Value Tender from 2022 –Bangladesh Transport Sector



## Invitation for Bids

https://www.adb.org/sites/default/files/tenders/ ban53382-wp-6a-ds-11-12a-ifb.pdf

Date:	7 December 2021
Loan No. and Title:	53382-BAN: South Asia Subregional Economic Cooperation Dhaka-Sylhet Corridor Road Investment Project
	LOT No. Part- 1: Construction Phase: Improvement of Dhaka - Sylhet National Highway (N2) into 4-Lane Highway with Service Lanes on Both Side from Sherpur Bridge Toll Plaza to Khasikapon Bazar End (Ch 186+700 to 200+800 km).
Contract No.	WP-6 Part- 2: Maintenance Phase: Performance Based Maintenance of Improved Dhaka - Sylhet National Highway (N2) for 6 Years from Sherpur Bridge Toll Plaza to Khasikapon Bazar End (Ch 186+700 to 200+800 km).
and Title:	LOT No. Part- 1: Construction Phase: Improvement of Dhaka - Sylhet National Highway (N2) into 4-Lane Highway with Service Lanes on Both Side from Khasikapon Bazar End to 7-Armed Police Battalion Headquarters, Lalabazar (Ch 200+800 to 211+900 km).
	DS- 12A Part- 2: Maintenance Phase: Performance Based Maintenance of Improved Dhaka - Sylhet National Highway (N2) for 6 Years from Khasikapon Bazar End to 7-Armed Police Battalion Headquarters, Lalabazar (Ch 200+800 to 211+900 km).
Deadline for Submission of Bids:	24 January 2022 14:00 hours and 14:30 hours (Bangladesh Standard Time)



## Sample High Value Tender from 2022 –Bangladesh Transport Sector

..Continued



 The Government of the People's Republic of Bangladesh (the Borrower) has applied for financing from the Asian Development Bank (ADB) towards the cost of "South Asia Subregional Economic Cooperation Dhaka-Sylhet Corridor Road Investment Project". Part of this financing will be used for payments under the contracts named above. Bidding is open to Bidders from eligible source countries of the ADB. https://www.adb.org/sites/default/files/tenders/ban53382-wp-6a-ds-11-12a-ifb.pdf

2. The Roads and Highways Department (RHD), the Executing Agency under Road Transport and Highways Division, Ministry of Road Transport and Bridges (MRTB), invites sealed bids from eligible Bidders for LOT No. Package No. Eligible Bidders can submit bids for one of the lots or both lots.

LOT No. DS- 11	<ul> <li>Part – 1: Construction Phase: Improvement of Dhaka - Sylhet National Highway (N2) into 4-Lane Highway with Service Lanes on Both Side from Sherpur Bridge Toll Plaza to Khasikapon Bazar End (Ch 186+700 to 200+800 km).</li> <li>Part – 2: Maintenance Phase: Performance Based Maintenance of Improved Dhaka - Sylhet National Highway (N2) for 6 Years from Sherpur Bridge Toll Plaza to Khasikapon Bazar End (Ch 186+700 to 200+800 km).</li> </ul>	<ul> <li>Which includes, but is not limited to the following works: <ul> <li>Flexible Pavement works with Modified Bitumen</li> <li>Earthwork in Road Embankment and Slope Protection</li> <li>Rigid Pavement in Service Lanes at Bus Bays</li> <li>Culverts – 10 Nos.</li> <li>Bridges - 6 Nos.</li> <li>Misc. works items of Sign Signal Guide Post, Road Marking etc.</li> </ul> </li> </ul>
LOT No. DS- 12A	Part – 1: Construction Phase: Improvement of Dhaka - Sylhet National Highway (N2) into 4-Lane Highway with Service Lanes on Both Side from Khasikapon Bazar End to 7 Armed Police Battalion Headquarters, Lalabazar (Ch 200+800 to 211+900 km).	

28 April 2025

### Sample High Value Tender from 2022 –Bangladesh Transport Sector



Part – 2: Maintenance Phase: Performance Based Maintenance of Improved Dhaka - Sylhet National Highway (N2) for 6 Years from Khasikapon Bazar End to 7 Armed Police Battalion Headquarters, Lalabazar (Ch 200+800 to 211+900 km).	<ul> <li>Rigid Pavement in Service Lanes, at Bus Bays</li> <li>Culverts – 15 Nos.</li> <li>Misc. works items of Sign Signal, Guide Post, Road Marking etc.</li> </ul>

 Completion time of the works from the commencement date for each Lot is 1460 days. Completion time for the Maintenance Phase works (Performance Based Maintenance works) from the end of defect notification period for each Lot is 2,190 days.

 Open Competitive Bidding (international advertisement) will be conducted in accordance with ADB's <u>Single-Stage: Two Envelope</u> bidding procedure and is open to all Bidders from eligible countries as defined in Bidding Document.

https://www.adb.org/sites/default/files/tenders/ban53382-wp-6a-ds-11-12a-ifb.pdf

- OCB = Open Competitive Bidding
- Prior = ADB reviewed bidding document
- 1S2E = Single Stage, 2-Envelope (Technical and Price Proposal)
- No. of Contracts = Invitation for 2 out of 3 Lots under the package

77

### Sample High Value Tender from 2022 –Bangladesh Transport Sector



..Continued

5. Only eligible Bidders with the following key qualification should participate in this bidding:

	LOT No. DS-11	LOT No. DS-12A
Average Annual Construction Turnover	The Bidder shall have minimum Average Annual Construction Turnover of USD 54 million for the contract calculated as total certified payments received for contracts in progress or completed within the last five (5) years.	The Bidder shall have minimum Average Annual Construction Turnover of USD 32 million for the contract calculated as total certified payments received for contracts in progress or completed within the last five (5) years.
Financial Resources	Requirement of minimum amount of liquid assets of the Bidder shall be USD 7 million for the contract.	Requirement of minimum amount of liquid assets of the Bidder shall be USD 4 million for the contract.
Construction Experience	Participated in at least one (1) Contract that has been successfully or substantially completed within the last seven (7) years and that is similar to the proposed highway standard road and structure works, where the value of the Bidder's participation exceeds USD 86 Million for the contract. The similarity of the Bidder's participation shall be based on the physical size, nature of works, complexity, methods, technology, or other characteristics as described in Section 6, Employer's Requirements. The complete eligibility and qualification requirements are stipulated in Section 3: Evaluation and Qualification Criteria.	Participated in at least one (1) Contract that has been successfully or substantially completed within the last seven (7) years and that is similar to the proposed highway standard road and structure works, where the value of the Bidder's participation exceeds USD 51 Million for the contract. The similarity of the Bidder's participation shall be based on the physical size, nature of works, complexity methods, technology, or other characteristics as described in Section 6. Employer's Requirements. The complete eligibility and qualification requirements are stipulated in Section 3: Evaluation and Qualification Criteria.

28 April 2025

# 77

## Sample High Value Tender from 2022 –Bangladesh Transport Sector





- To purchase the Bidding Document in English, eligible Bidders should:
  - Write to the address above requesting the required Bidding Document by quoting the contract number and title and during normal office hours on all working days up to the day before the submission deadline
  - pay a nonrefundable fee of Tk. 10,000 in cash for each lot. The Bidding Document may also be sent via courier for an additional fee of Tk. 50,000 for overseas delivery only. No liability will be accepted for loss or late delivery of the Bidding Document.

 A Pre-Bid meeting will be held at the office of the Chief Engineer's Conference Room, Sarak Bhaban, Tejgaon, Dhaka. Bangladesh on 27 December 2021 at 12:00 hours (Bangladesh Standard Time).

- 9. Deliver your bid
  - to the address above
  - on or before the bid submission deadline: Date: 24 January 2022 at 14:00 hours for Lot No. DS-11 and at 14:30 hours for Lot No. DS-12A (Bangladesh Standard Time).
  - All bids must be accompanied by a Bid Security in the amount as stated in the Bidding Document (Bid Data Sheet). Late Bids shall be rejected.

10. The Technical Proposal of the Bids for Lot No. DS-11 will be opened at 14:15 hours and for Lot No. DS-12A will be opened at 14:45 hours (Bangladesh Standard Time) at the address above on 24 January 2022 in the presence of the Bidders' representatives who choose to attend. The price proposal of responsive Bids will be opened in presence of the Bidder's authorized representative who choose to attend at the time, date and address to be advised by the Employer after approval of the Technical Bid Evaluation Report by the Employer with no objection from ADB.

#### https://www.adb.org/sites/default/files/tenders/ban53382-wp-6a-ds-11-12a-ifb.pdf

## Consulting **Opportunities** from adb.org Firm & Individual Consulting

https://www.adb.or g/projects/tenders/ country/banglades h/type/firmconsulting-1566/type/individu al-consulting-1516

Projects & Tenders	Projects Documents	Tenders	
Filter results CLEAR		Q. Key Document	AD
Country/Economy (1)	Search tenders	C Key Document	5
(CLEAR)	Results 1-20 of 1827	RSS Sort by - Procurement Plan	i i
Regional Afghanistan	a Bangladesh X Firm - Cons X Individual X	Procurement Polic	У
Armenia Armenia Azerbajan Bangladesh	project management, supervision and status: institutional development consultant Active 57188-001; Bangladesh; Water and other urban infrastructure	Deadline: Procurement Regu 02 Jun 2025 nd services; Posting	lations
Bhutan Bhunel Darussalam	date: 21 Apr 2025 Notice Type: Firm - Consulting	Shortlisted F Consulting S	And the second se
Sectors	<ul> <li>National Individual Consultant as Quantity grans:</li> <li>Surveyor-1 &amp; 2 (2 Expert Positions) Active</li> </ul>	Deadline: 04 May 2025 See the list -+	
Apriculture, natural resources and rural development	53260-001; Bangladesh; Industry and trade; Posting date: 17 A Notice Type: Individual - Consulting	Archive: Co	ntracts
Education Energy	National Individual Consultant as Site Engineer-1 & 2 (2 Expert Positions) Active 53260-001; Bangladesh; Industry and trade; Posting date: 17 A	Deadline: Awarded - O 04 May 2025 Works, and 2 or 2025	
Finance Health	Notice Type: Individual - Consulting	Set the lid ++	
linduitry and trade	National Financial Management Consultant Super-	Deadine Business Ce	otor
Type (2) [CLEAR]	<ul> <li>53260-001; Bangladesh; Industry and trade; Posting Closed date: 15 Apr 2025</li> </ul>	21 Apr 2025 All you need to w	
Contracts Awarded	Notice Type: Individual - Consulting	one place>	
Firm - Consulting	National Individual Consultant as Project Statut Manager Closed	Deadline 24 Apr 2025 Advisory: Be	ware of
Invitation for Bids	53260-001; Bangladesh; Industry and trade; Posting date: 07 A	v 2025 business sca	ms using
Other Notice Pregualified applicants	Notice Type: Individual - Consulting	ADB's name Read more -+	


28 April 2025

ADB <sup>Consultant Management System</sup>	Home Consulting Opportu	nilies Shortlisted Firms	Awarded	Contracts TA	Claims Partne	r Consul	ant Tulor
Consulting Opportunities							
Consulting Services Recruitment Notices (CSRN)							
CSRN provides detailed information on the consulting interest by ticking the appropriate checkboxes or by e		ninistered projects, inclu	iding terms o	f reference. Filt	er on specific	c advertisem	ents of
Refine by Clear All	Search by Expertise			Go			
Consultant Type	Search by Experuse			Engagement	1	Deadline	
Firm (42)	Project	Expertise	Consultant Type		Published	(Manila local time)	View CSRN
Individual (163)	LOAN 57188-001 BAN: Khuina Water Supply Project (Phase 2) - KWASA/KWSP-	Project Management, construction supervision	Firm	48	21-Apr-2025	02-Jun-	
- Eligibility of Consultant Country	2/5-01 project management, supervision	and institutional				2025 11:59 PM	4
Open to Member Countries Only (204)	and institutional development consultant	development for water supply service					
<ul> <li>Non-Member Countries Allowed (1)</li> </ul>	TA 59115-001 BAN: UPS project feasibility study firm under the TA : Building Capacity	Feasibility study	Firm	15	26-Apr-2025	10-May- 2025 11:59	178
_ Engagement Period	for Universal Pension Schemes (attached TA)					PM	101
Less than 3 months (7)	TA-10435 REG: Enhancing Asia and the Pacific's Readiness for Resilient Disaster	; Resilient Disaster Recovery	Firm	40	09-Apr-2025	03-May- 2025 11:59	191
3 months to 1 year (121)	Recovery (58318-001)					PM	10
More than 1 year (77)	LOAN 57296-002 BAN: South Asia Subregional Economic Cooperation:	Consultancy Services for Construction Supervision	Firm	48	05-Mar-2025	02-May- 2025 11:59	-
	Chattogram-Dohazan Railway Project - SD 1 Consultancy Services for Construction					PM	-
Country	Supervision						

## Subscribe to receive alerts\* for Goods/Works - <u>https://alerts.adb.org</u>

Subscribe to ADB's Newsletters, Alerts and RSS feeds.		Follow ADB: 💟 🕨 🖪 🚥	0 in
Articles and Videos	On Off	Events	On Off
Asian Development Blog	On Off	News Releases and News from Country Offices	on Off
Board Documents	on on	Procurement Notices (Goods and Works) Hote Weekly relifications on consuling opportunities available for registered uses of the <u>Consultant</u> Monotement Section (CMS).	On Off
Business Center Materials	On Off	Project Information and Documents	On Off
Country Planning Documents	On Off	Publications	On Off
Economic Data and Research	on off	Safeguard Documents	On Off
Evaluation Reports	On Off	Vacancies	On Off

### Consulting services alerts received through <u>http://csrn.adb.org</u>



## Registration in Consultant Management System (CMS)

## Advisory

# http://cms.adb.org

Due to scheduled maintenance, CMS access will be intermittent on Saturday, 30 November 2024 from 8 a.m. until 1 p.m. (Manila time). Any use of CMS during this time may be interrupted. For inquiries, please

contact cmshelp@adb.org

### Registration also required for Executing Agency





28 April 2025

(EA)



	ADB Consultant Management System           Home         Consultang Opportunities         Shortisted Firms         Awarded Contracts         TA Claims Partner         Consultant Tutor           LOAN 571t88-001 BAN: Khulna Water Supply Project (Phase 2)         KWA SA KWSP-2/S-01 project management, supervision and institutional development consultant         Consultant Tutor         Consultant Tutor	B
http://cms .adb.org (Open View for All)	Deadline     Deadline	nit OI es
	Contact Information Contact Information Project Officer Email Md. Husain Sawkat Khulna Water Supply and Sewerage Authority Contact Details CSRN Additional Information / Attachments	
Executing Agency	Title     Type     Description     Category     Last Updated By     Last Updated     Update     Delete       No results found.     Agencies	
28 April 2025	Primary       Agency       Country       Agency Role       Contact Person       View Detail         M       Khulna Water Supply and Sewerage Authority       Bangladesh       Executing Agency       Imagency       Imagency         ADB Business Opportunities Seminar       Imagency       Imagency       Imagency       Imagency       Imagency	42



CMS Reg Continue	gistration in <sub>.</sub> ed	http://cm	<u>s.adb.org</u>	
ADB Consultant Management System				
Basic information			Adaptiments and Cartification	
Emplified Registration + Indicates required field NOTE: Complete the regulation within 35 minutes to avoid loang data. Please review	w the form and assemble residued information prior to Min	g in the regulation.		Cancel Date Information • Continue
Deportant By proving your consuling wetty's details, you are agreent to <u>ACP 1 use of your</u> Beautyman, they Golds.	where where the state of the st	You are also settlying that the offernal	torish decidants and that to the last of your knowledge. To	tion more in two to repeter, downland <u>Consultane Edity</u>
Dervall Recolum Description				
* Deerall Revealed Description of the Print/Organisation Huma Initia 200 multi- Huma Initia		The Louisty of Incorporation/Register	from you have selected below is not among the <b>lat of ADB</b>	creatible; countries Them you are only allowed to express interest in
of the Print/Organization Huma lost to 300 mints. Flatts/Degastization Information			•	
of the Print/Organization Huma lot to 300 multi. Flets/Degasization Information By providing the recorporation/registration ditails below, you are agreeing to addre				
of the Pres/Organization Huma lost to 300 mmin. Fless/Organization Information By providing the econoporation/registration dotain below, you are agreeng to addre opportunities open to non-member countries defined as part of project regumented	* Country of Securporation/Registration * Year of Securporation/Registration Decemporation Document or Registration Number		•	
of the Pres/Organization Huma lost to 300 mmin. Fless/Organization Information By providing the econoporation/registration dotain below, you are agreeng to addre opportunities open to non-member countries defined as part of project regumented	* Country of Securporation/Registration * Year of Securporation/Registration Decemporation Document or Registration Number pertil completed from year of incorporation/registration			
of the Pres/Organization Huma lost to 300 mmin. Fless/Organization Information By providing the econoporation/registration dotain below, you are agreeng to addre opportunities open to non-member countries defined as part of project regumented	* Country of Encorporation/Registration * Here of Encorporation/Registration Decorporation/Decument or Registration Number gette completed from your of incorporation/registration * Type of Departuration		•	
of the Pres/Organization Huma lost to 300 mmin. Fless/Organization Information By providing the econoporation/registration dotain below, you are agreeng to addre opportunities open to non-member countries defined as part of project regumented	* Country of Securporation/Registration * Year of Securporation/Registration Decemporation Document or Registration Number pertil completed from year of incorporation/registration			
of the Pres/Organization Huma ker to bit work. Firm/Organization Information by providing the recorporation/repstation datata below, you are agreen to adver opportunities open to non-member countries defined as part of project requirement Number of pro- * laryour orga	* Country of Securporation/Registration * Year of Securporation/Registration Decemporation Document or Registration Number gette completed from year of incorporation/registration " Type of Organization * Number of permanent NII-line professional staff	V con regeneration in incomposition for one control       O train     O train       O train     O train       O train     O train       D train     O train		
of the Pres/Organization Huma ker to bit work. Firm/Organization Information by providing the recorporation/repstation datata below, you are agreen to adver opportunities open to non-member countries defined as part of project requirement Number of pro- * laryour orga	Country of Encorporation/Registration     * Year of Encorporation/Registration     Discorporation/Document or Registration Number gets completed from year of incorporation/registration     * Type of Organization     * Number of permonent hal-kine professional shaft     * Han year organization ever been engaged by ADBP mobility a government-owned institution; click on this icon; pi	Prior regeneration in incrementaria on reservant O Train O Train O Train O Train Prior opportunition increment Drain O Train O Train O Train	O International Contactual	

# 77

# Useful Links




- ADB Procurement Policy: <u>https://www.adb.org/documents/adb-procurement-policy</u>
- ADB procurement Regulations: <u>https://www.adb.org/documents/procurement-regulations-adb-borrowers</u>
- Guidance Notes: <u>https://www.adb.org/documents/guidance-notes-on-procurement</u>
- Standard Bidding Documents and User Guides: <u>https://www.adb.org/business/main</u> (Scroll to Documents and Forms)
- ADB Consultant Management System: <a href="http://cms.adb.org">http://cms.adb.org</a>
- ADB Anticorruption and Integrity: <a href="http://www.adb.org/site/integrity/main">www.adb.org/site/integrity/main</a>
- ADB BOS 2024 for Bangladesh: <u>https://events.development.asia/learning-events/adb-business-opportunities-seminar-bangladesh-2024</u>

# **Support Activities - eLearning**

https://elearn.adb.org/login/index.php

• 10 eLearning Modules (20 to 40min per module): • Module 1: Overview of the Procurement Framework Module 2: Strategic Procurement Planning Module 3: Risk Management ADB O Module 4: Analysis • Module 5: Procurement Strategy Development • Module 6: Bidding Procedures • Module 7: Consulting Services ○ Module 8: Bid Evaluation Module 9: Contract Management ○ Module 10: FCAES











*For further information/ query/ comment/ suggestion:* 

Lila Dhyana Mallory, Senior Procurement Specialist Imallory@adb.org

Mohammed Zulyaminayn, Principal Procurement Officer <u>mzulyaminayn@adb.org</u>

Md. Rasel Parvez, Procurement Officer mparvez@adb.org
